

ENGINEERING CIP REPORT - December 2019

PROJECT				STATUS / COMMENTS		CONST. DATES
ROADS	CITY	1	2019 Street and Alley Rehabilitation (Various Locations)	ST1906	COMPLETE	Substantially Complete
		2	Allen Drive Gateway Project (US 75 Interchange)	ST1903	1st submittal received & under review for roadway Parks Department has negotiated the landscape design contract.	TBD
		3	Bethany & Heritage Traffic Signal Improvement	ST1907	Construction ongoing.	Complete Winter 2019
		4	Traffic Signal Detection Equipment	ST1908	Contract is executed by Austin. 60% comment from TXDOT will be received Monday , Dec 02	Complete Summer 2020
		5	2020 Street and Alley Rehabilitation (Various Locations)	ST2002	Gathering location list & generating bid docs	TBD
		6	Mcdermott - Twin Creek & Suncreek Intersection	ST1909	Architect is working on the concept plan for sign relocation from median to SW corner on Suncreek Dr.	Complete Summer 2020
		7	Median Improvement Project (Select Medians)	ST1705	Contractor is completing punch list items	Complete
	OTHERS	8	FM 2551 (Main - Parker Rd)	ST0316	Design of widening to 6-lanes. NTMWD and TxDOT have reached an agreement on design conditions. TxDOT has provided plans for City to review.	2022
		9	Ridgeview / US 75 Overpass	TXDOT	Preliminary Engineering and project is environmentally clear. Two bypass lanes on the southbound frontage road will be provided. TxDOT holding utility relocation meetings.	2022
UTILITIES & DRAINAGE	CITY	10	Allenwood Drainage	DR1901	Waterline portion 90% complete. Drainage portion advertises for bid December 5th	Early 2020
		11	Bethany Tower & Stacy Ground Storage Tank #3 Repaint	WA1903	Stacy Tanks phase has been completed. Bethany Tanks, all Equipment is now on Site for work and construction of shroud has begun. Work will be completed March of 2020	Complete March 2020
		12	Custer & Stacy Flow Meter Replacement	WA1903	Bidding process ended, sources are being contacted. Will go to Council January 24th 2020.	Jun-20
		13	Hillside Water & Sanitary Sewer Rehabilitation, PH 2	WA1902	Utility construction complete and pavement restoration is underway.	Complete March 2020
		14	Sloan Creek Regional Sewer	WA1904	Council authorized to begin negotiation for easement purchase - 60% plan comments returned to consultant	2020
		15	Stacy Pump Station Rehab	WA1906	PSE proposal received & is under review - anticipated design contract award January 2020	2020
		16	Water & Sewer Improvements - Greenville/Chaparral & Main/Boyd	WA1802	Under construction	Complete March 2020
		17	CBD - RR Sanitary Sewer Improvements	WA1908	Project is under design to replace the aging sanitary sewer and allow for future development.	TBD
	18	Windridge Water & Sanitary Sewer Rehabilitation, PH 1 & 2	WA1901	60% design plans reviewed & sent back to consultant for revisions	2020	
	OTHERS	19	Rowlett Creek Sewer Extension	NTWMD	Utility work complete & NTMWD's contractor is working on remaining punchlist items	Complete December 2019
OTHER	20	Central Fire Remodel & Expansion	PS1701	Phase 1 95% finished, external trellis and landscape work has begun, Phase 1 completion by Jan 10, 2020	Complete Fall 2020	

CONSTRUCTION


DESIGN

DESIGN (BY OTHERS)

CONSTRUCTION (BY OTHERS)

FUTURE

ENGINEERING CIP MONTHLY REPORT

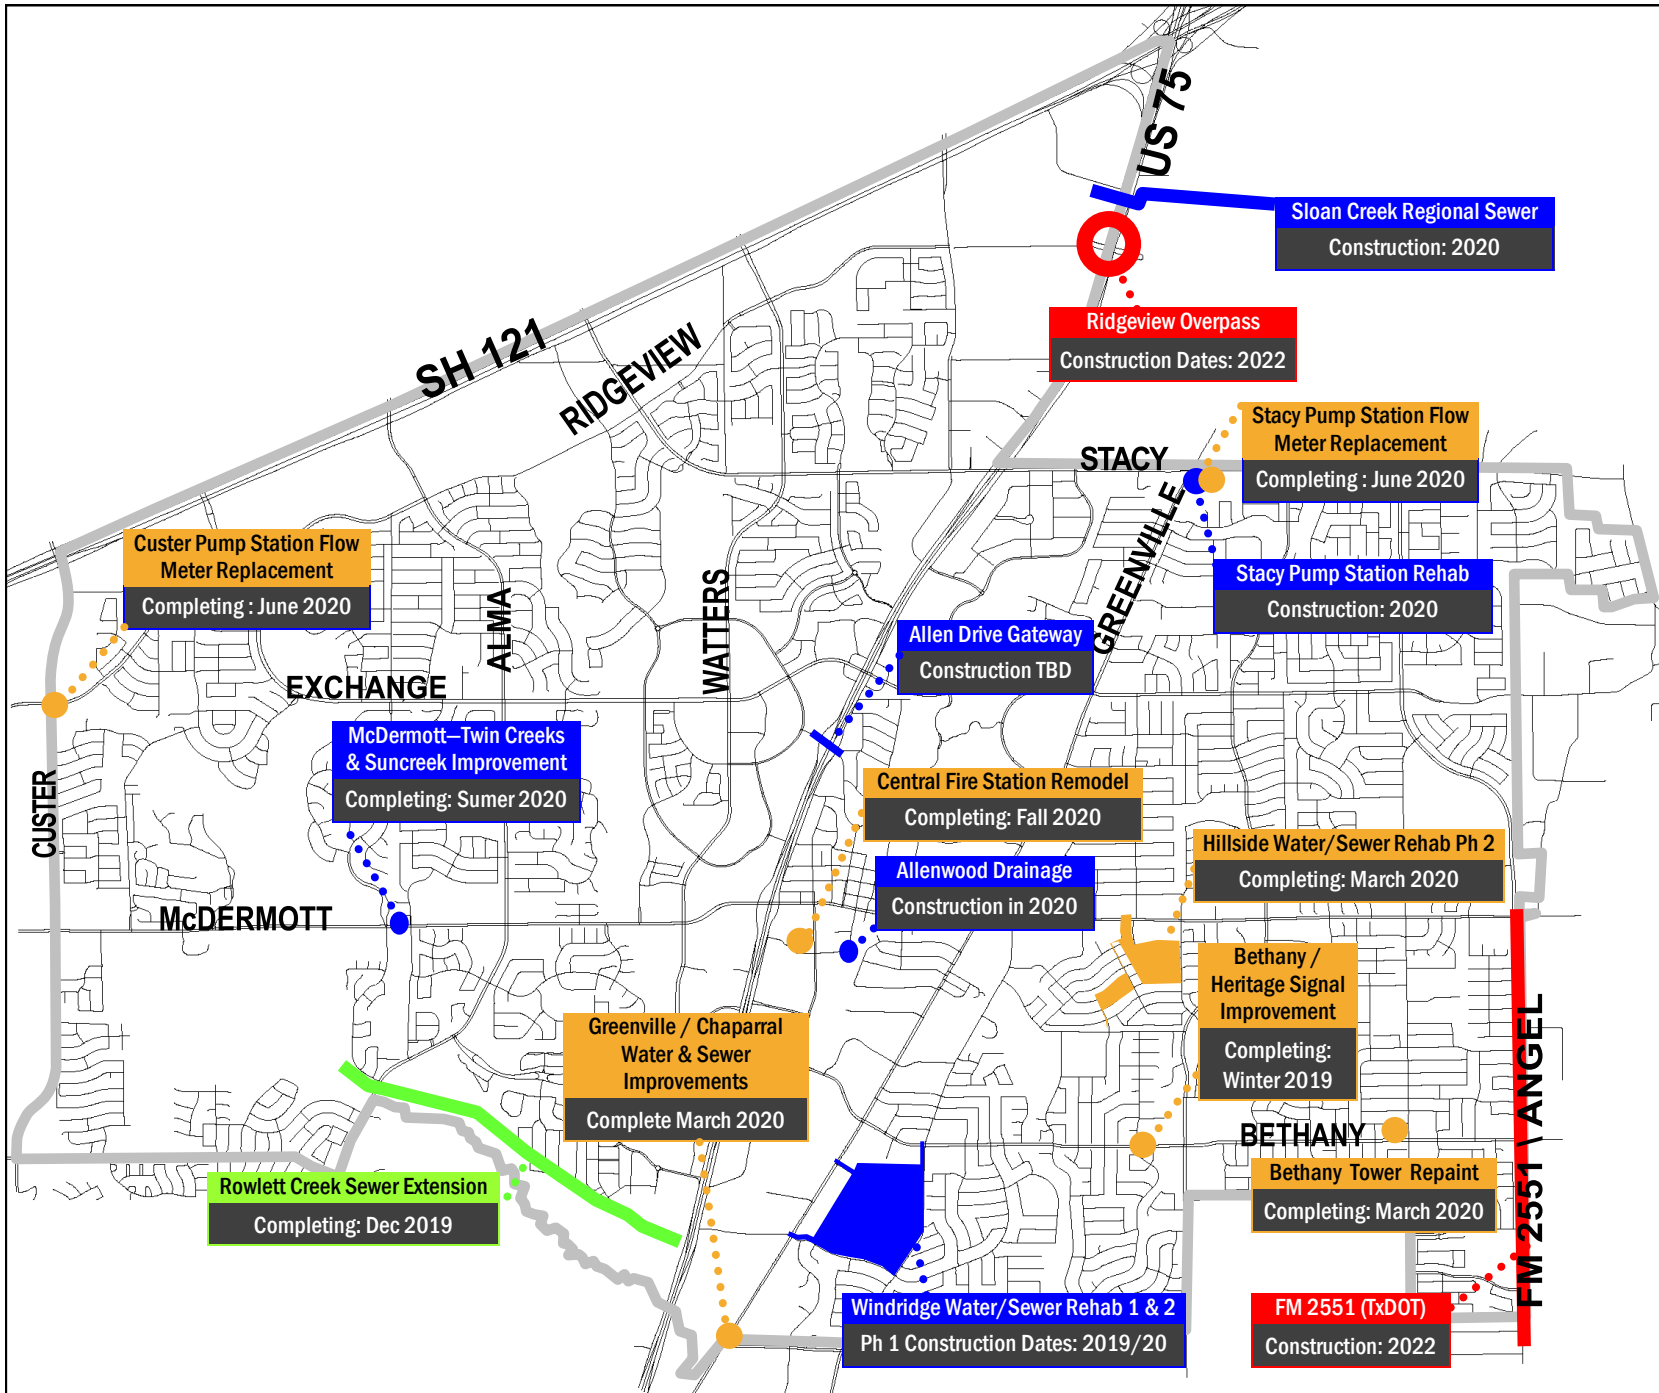

December
2019

CONSTRUCTION

DESIGN

CONSTRUCTION
(By Others)

DESIGN
(By Others)

FUTURE

ENGINEERING
DEPARTMENT
214.509.4576

DIRECTOR:
CHRIS
FLANIGAN

