


ENGINEERING CIP MONTHLY REPORT

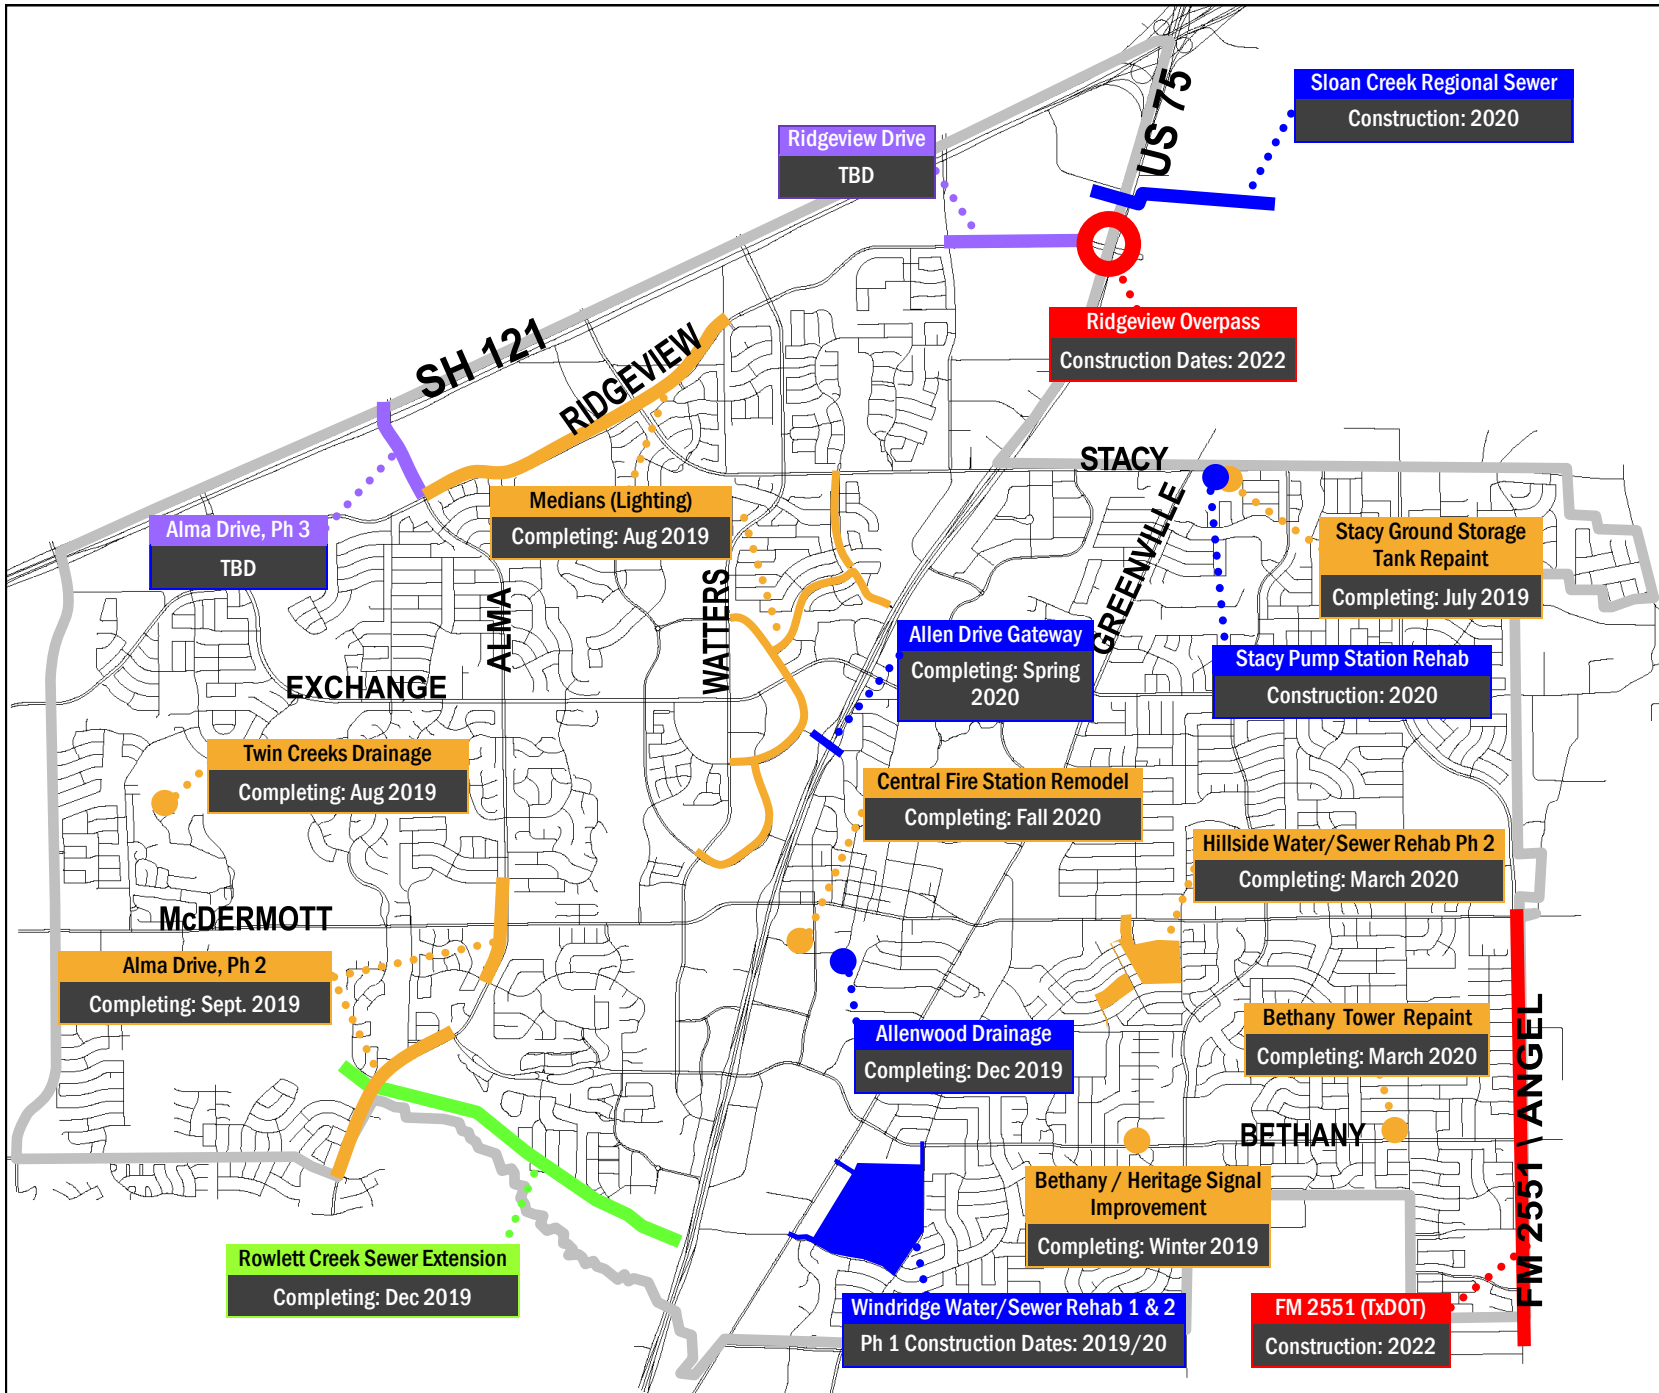

**AUG
2019**

CONSTRUCTION

DESIGN

**CONSTRUCTION
(By Others)**

**DESIGN
(By Others)**

FUTURE

**ENGINEERING
DEPARTMENT
214.509.4576**

**DIRECTOR:
CHRIS
FLANIGAN**



ENGINEERING CIP REPORT - THROUGH AUGUST 2019

PROJECT				STATUS / COMMENTS		CONST. DATES
ROADS	CITY	1	2018 Street and Alley Rehabilitation (Various Locations)	ST1804	Finishing up restoration and punch-list items.	COMPLETE
		2	2019 Street and Alley Rehabilitation (Various Locations)	ST1906	Improvements with school traffic impacts have begun.	Nov-19
		3	Allen Drive Gateway Project (US 75 Interchange)	ST1903	PS&E design has begun. Parks Department is negotiating design contract for landscape architecture.	Complete Spring 2020
		4	Alma Drive Improvements, PH 2 (Hedgcoxe-Rainforest)	ST1503	Contractor is paving the right turn lanes at McDermott that were delayed by franchise utilities. The utility conflicts delayed the construction by 2 months. Expected completion is September 2019	September 2019
		5	Bethany & Heritage Traffic Signal Improvement	ST1907	Project is out for bid. Bid opening is August 29	Complete Winter 2019
		6	Traffic Signal Detection Equipment	ST1908	City Council approved April 9, 2019 purchase order request for 5 detection equipment	Summer 2020
		7	Median Improvement Project (Select Medians)	ST1705	Working with Oncor on last transformer set at Stockton and Curtis. Project completion end of August 2019	Complete Summer 2019
	OTHERS	8	FM 2551 (Main - Parker Rd)	ST0316	Design of widening to 6-lanes. NTMWD and TxDOT have reached an agreement on design conditions. Detailed design now able to resume.	2022
		9	Ridgeview / US 75 Overpass	TxDOT	Preliminary Engineering and project is environmentally clear. Two bypass lanes on the southbound frontage road will be provided. TxDOT holding utility relocation meetings. Waterline has been advertised for construction.	2022
UTILITIES & DRAINAGE	CITY	10	Allenwood Drainage	DR1901	Once waterline is underconstruction Staff will re-bid the drainage work.	Complete December 2019
		11	Bethany Tower & Stacy Ground Storage Tank #3 Repaint	WA1903	Stacy Tanks phase has been completed. Bethany Tanks have been awarded and are to start no earlier than November 15th.	Complete Spring 2020
		12	Hillside Water & Sanitary Sewer Rehabilitation, PH 2	WA1902	Utility construction underway and some restoration has begun.	Complete March 2020
		13	Sloan Creek Regional Sewer	WA1904	Survey complete, working on final alignment with NTMWD to proposaed lift station and easement acquisition	2020
		14	Stacy Pump Station Rehab	WA1906	Engineer has been hired for the first phase of site evaluation and recommendations development. Initial report due later in July.	Fiscal Year 2020
		15	Twin Creeks Drainage	DR1804	Project will be closed out end of August.	Substantially Complete
		16	Windridge Water & Sanitary Sewer Rehabilitation, PH 1 & 2	WA1901	Initial review comments returned to the consultant for revisions	TBD
	OTHERS	17	Rowlett Creek Sewer Extension	NTWMD	NTMWD's contractor has completed the pipe installation and is working towards restoration items.	Complete Dec 2019
OTHER	18	Central Fire Remodel & Expansion	PS1701	Foundation complete and going vertical. Phase 1 to be complete January 2020. Phase 2 scheduled to begin January 30, 2020.	Complete Fall 2020	

CONSTRUCTION

DESIGN

DESIGN (BY OTHERS)

CONSTRUCTION (BY OTHERS)

FUTURE
