


# ENGINEERING CIP REPORT - SEPTEMBER 2019

| PROJECT              |        |    |   | STATUS / COMMENTS |   | CONST. DATES            |
|----------------------|--------|----|---|-------------------|---|-------------------------|
| ROADS                | CITY   | 1  | 2019 Street and Alley Rehabilitation (Various Locations)      | ST1906            | Working through locations   | November 2019           |
|                      |        | 2  | Allen Drive Gateway Project (US 75 Interchange)               | ST1903            | PS&E design has begun. Parks Department is negotiating design contract for landscape architecture.  | Complete Spring 2020    |
|                      |        | 3  | Aylesbury Drive Improvement Project                           | ST1905            | Contractor has completed pavement removal, lime and will be setting grade.  | Complete September 2019 |
|                      |        | 4  | Alma Drive Improvements, PH 2 (Hedgcoxe-Rainforest)           | ST1503            | Construction is expected to be substantially complete by middle September 2019.   | Complete September 2019 |
|                      |        | 5  | Bethany & Heritage Traffic Signal Improvement                 | ST1907            | Project is out for bid. Bid opening is August 29 . Traffic Signal poles were ordered beginning of August.   | Complete Winter 2019    |
|                      |        | 6  | Traffic Signal Detection Equipment                            | ST1908            | LAPFA Aggement signed by City of Allen. Signed contract is send to TXDOT Dallas District. Sole Source is approved for the equipment puchase. TXDOT requires cost estimate for the equipments. | Complete Summer 2020    |
|                      |        | 7  | Median Improvement Project (Select Medians)                   | ST1705            | Oncor delivered the wrong transformer at Stockton and Curtis and had to order a new one.  | Complete Summer 2019    |
|                      | OTHERS | 8  | FM 2551 (Main - Parker Rd)                                    | ST0316            | Design of widening to 6-lanes. NTMWD and TxDOT have reached an agreement on design conditions. Detailed design now able to resume.  | 2022                    |
|                      |        | 9  | Ridgeview / US 75 Overpass                                    | TXDOT             | Preliminary Engineering and project is environmentally clear. Two bypass lanes on the southbound frontage road will be provided. TxDOT holding utility relocation meetings.                   | 2022                    |
| UTILITIES & DRAINAGE | CITY   | 10 | Allenwood Drainage  | DR1901            | Waterline portion will be presented to Council for award on September 10th.   | TBD                     |
|                      |        | 11 | Bethany Tower & Stacy Ground Storage Tank #3 Repaint          | WA1903            | Stacy Tanks phase has been completed. Bethany Tanks have been awarded and are to start no earlier than November 15th.   | Complete March 2020     |
|                      |        | 12 | Hillside Water & Sanitary Sewer Rehabilitation, PH 2          | WA1902            | Utility construction wrapping up and pavement restoration has begun.  | Complete March 2020     |
|                      |        | 13 | Sloan Creek Regional Sewer                                    | WA1904            | Finalizing the alignment and working on easement acquisition documents / appraisal  | 2020                    |
|                      |        | 14 | Stacy Pump Station Rehab                                      | WA1906            | Site evaluation and recommendation report complete & consultant is addressing coments & generating a future timeline for moving forward. Schedule anticipated mid September.                  | Fiscal Year 2020        |
|                      |        | 15 | Twin Creeks Drainage  | DR1804            | Project is substantially complete awaiting to establish grass.  | Substantially Complete  |
|                      |        | 16 | Water & Sewer Improvements - Greenville/Chaparral & Main/Boyd | WA1802            | Project Advertised on Aug 22. Award anticipated in September  | TBD                     |
|                      |        | 17 | CBD - RR Sanitary Sewer Improvements                          | WA1908            | Project is under design to replace the again sanitary sewer and allow for future development  | TBD                     |
|                      | OTHERS | 18 | Windridge Water & Sanitary Sewer Rehabilitation, PH 1 & 2     | WA1901            | 60% design plans received for both project phases and are under review  | Substantially Complete  |
|                      |        | 19 | Rowlett Creek Sewer Extension                                 | NTWMD             | Utility work complete & NTMWD's contractor is working on remaining restoration items.   | Complete December 2019  |
| OTHER                |        | 20 | Central Fire Remodel & Expansion                              | PS1701            | Foundation complete and going vertical. Phase 1 to be complete January 2020. Phase 2 scheduled to begin January 30, 2020.   | Complete Fall 2020      |

CONSTRUCTION
DESIGN
DESIGN (BY OTHERS)
CONSTRUCTION (BY OTHERS)
FUTURE

# ENGINEERING CIP MONTHLY REPORT

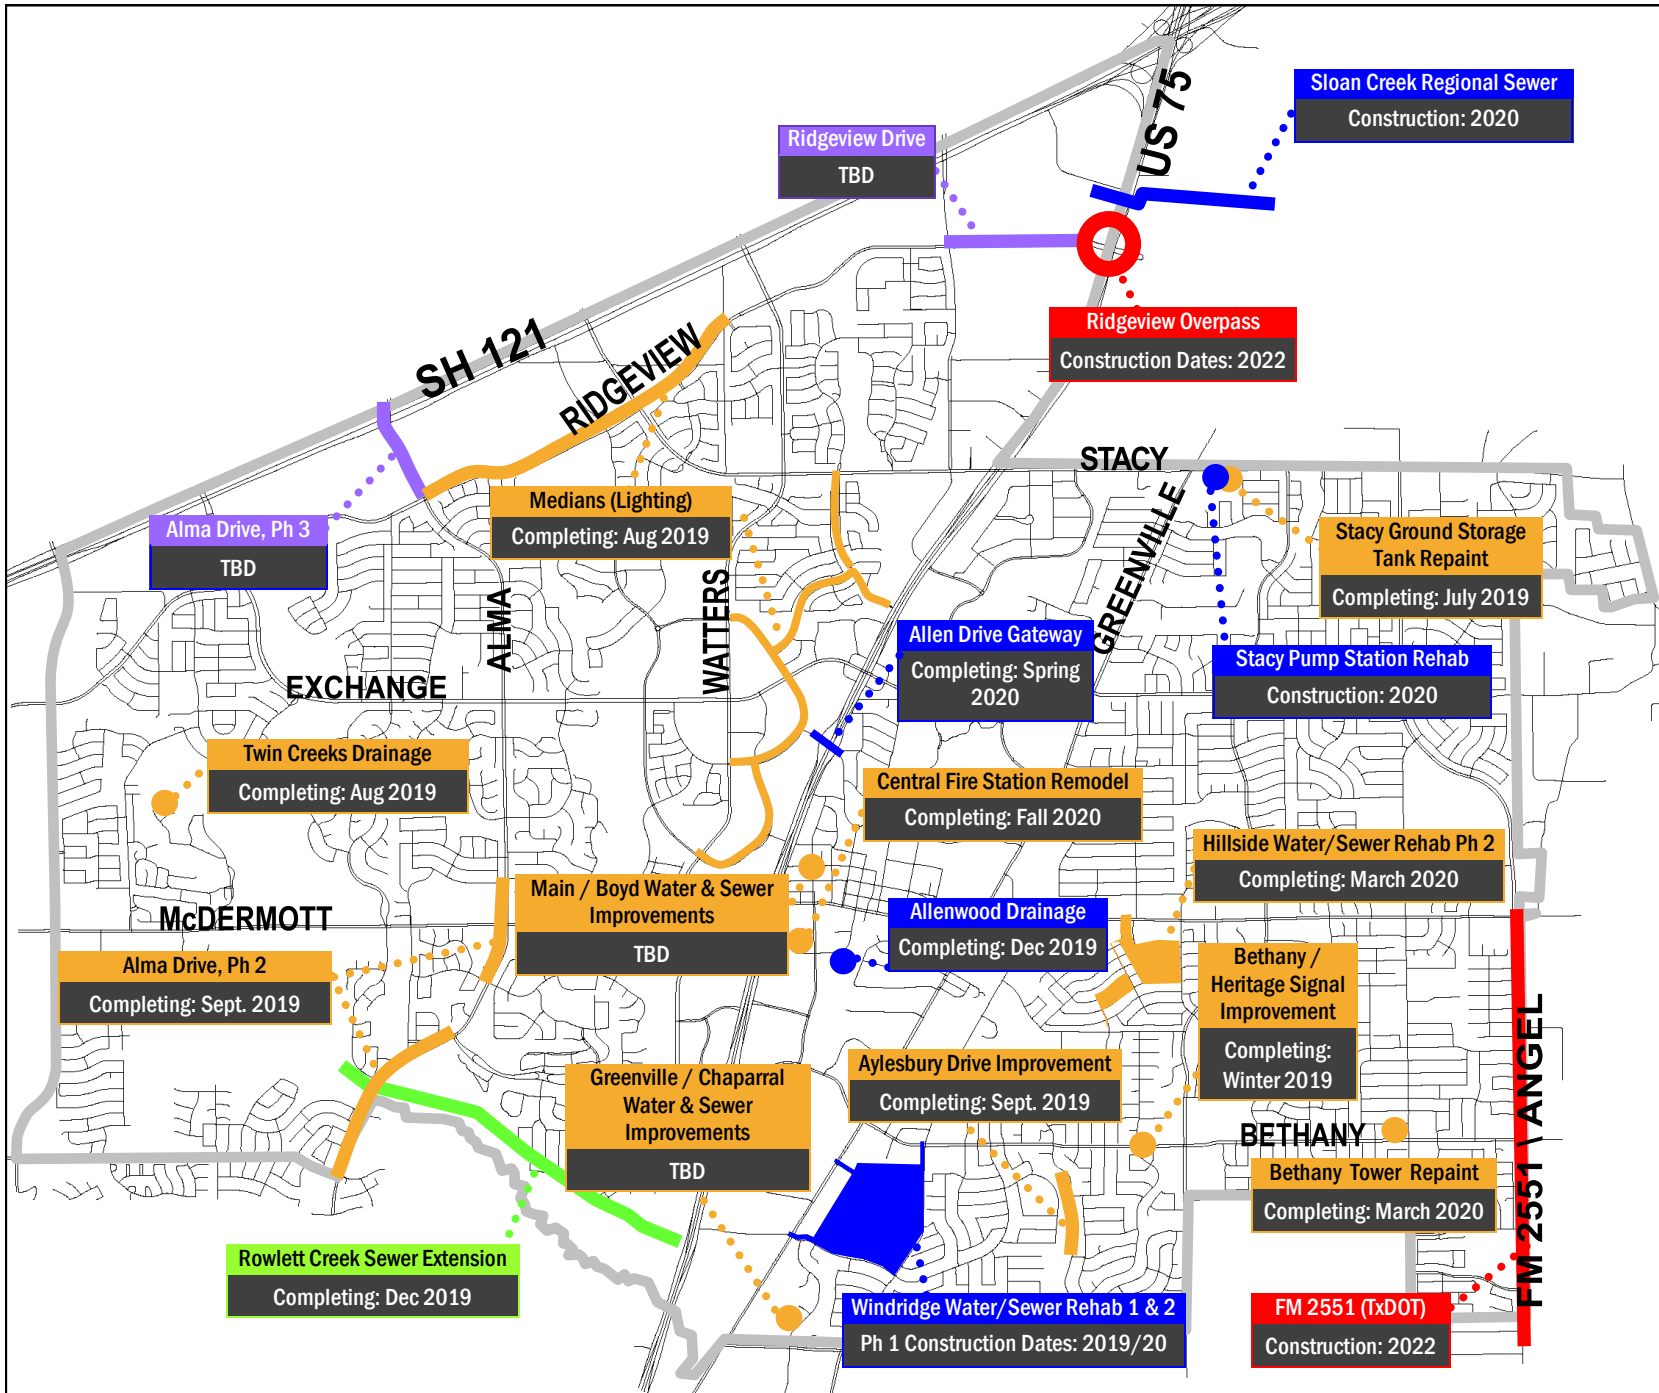

**SEPT  
2019**

**CONSTRUCTION**

**DESIGN**

**CONSTRUCTION  
(By Others)**

**DESIGN  
(By Others)**

**FUTURE**

**ENGINEERING  
DEPARTMENT  
214.509.4576**

**DIRECTOR:  
CHRIS  
FLANIGAN**

