

ENGINEERING CIP REPORT - February 2020

PROJECT				STATUS / COMMENTS		CONST. DATES
ROADS	CITY	1	Allen Drive Gateway Project (US 75 Interchange)	ST1903	TxDOT has been submitted the 60% design plans Parks Department is working with DCBA on Phase 1 landscape design	TBD
		2	Bethany & Heritage Traffic Signal Improvement	ST1907	City Attorney Sent Letter to Bonding Agency (Surety) and Contractor (World fiber) for Default of the Contract. Will Need a New Contractor for the Project	TBD
		3	Traffic Signal Detection Equipment	ST1908	95% Plan submitted to TxDOT Jan 6, 2020. The project will be Bid by TxDOT with City of Frisco and City of Denton	Complete Summer 2020
		4	2020 Street and Alley Rehabilitation (Various Locations)	ST2002	Finalizing Construction Documents.	TBD
		5	Mcdermott - Twin Creek & Suncreek Intersection	ST1909	New Idea for unsplitting the intersectionconceived. New Suncreek sign will be constructed in the new shifted median.	Complete Summer 2020
	OTHERS	6	FM 2551 (Main - Parker Rd)	ST0316	Design of widening to 6-lanes. NTMWD and TxDOT have reached an agreement on design conditions. City has provided plan comments back to TxDOT	2022
		7	Ridgeview / US 75 Overpass	TxDOT	Preliminary Engineering and project is environmentally clear. Two bypass lanes on the southbound frontage road will be provided. City Provided 30% Comments to TxDOT.	Jul-05
UTILITIES & DRAINAGE	CITY	8	Allenwood Drainage	DR1901	Council Awarded contract. Working with contractor to set up Pre-Construction Meeting	Early 2020
		9	Bethany Tower & Stacy Ground Storage Tank #3 Repaint	WA1903	Stacy Tank has been completed. Bethany Tank site, the shroud is in place and the tank is drained. Work will be completed March of 2020	Complete March 2020
		10	Custer & Stacy Flow Meter Replacement	WA1903	Council Awarded contract. Working with contractor to set up Pre-Construction Meeting.	Complete June 2020
		11	Hillside Water & Sanitary Sewer Rehabilitation, PH 2	WA1902	Contractor working on Final construction items. Council Awarded Micro Seal to be completed in the spring 2020	Complete March 2020
		12	Sloan Creek Regional Sewer	WA1904	Initial Offer Letters for easement acquisition have been mailed.	Jul-05
		13	Stacy Pump Station Rehab	WA1906	Council Awarded Contract. Engineer has begun PS&E design	Jul-05
		14	Water & Sewer Improvements - Greenville/Chaparral & Main/Boyd	WA1802	Under construction	Complete March 2020
		15	CBD - RR Sanitary Sewer Improvements	WA1908	Project is under way with design to replace the aging sanitary sewer pipes and increase the size to allow for future development.	TBD
		16	Windridge Water & Sanitary Sewer Rehabilitation, PH 1 & 2	WA1901	Consultant to provide 90% plans for Phase 1 and 2	Jul-05
	OTHERS	17	Rowlett Creek Sewer Extension	NTWMD	Project is in the Closeout Phase with NTMWD	Substantially Complete
OTHER	18	Central Fire Remodel & Expansion	PS1701	Waiting for startup by 3rd party USDD, New Firehouse occupied and operational. Phase 2 demolition of 2nd floor Administration Building has begun.	Complete Fall 2020	

CONSTRUCTION


DESIGN

DESIGN (BY OTHERS)

CONSTRUCTION (BY OTHERS)

FUTURE

ENGINEERING CIP MONTHLY REPORT

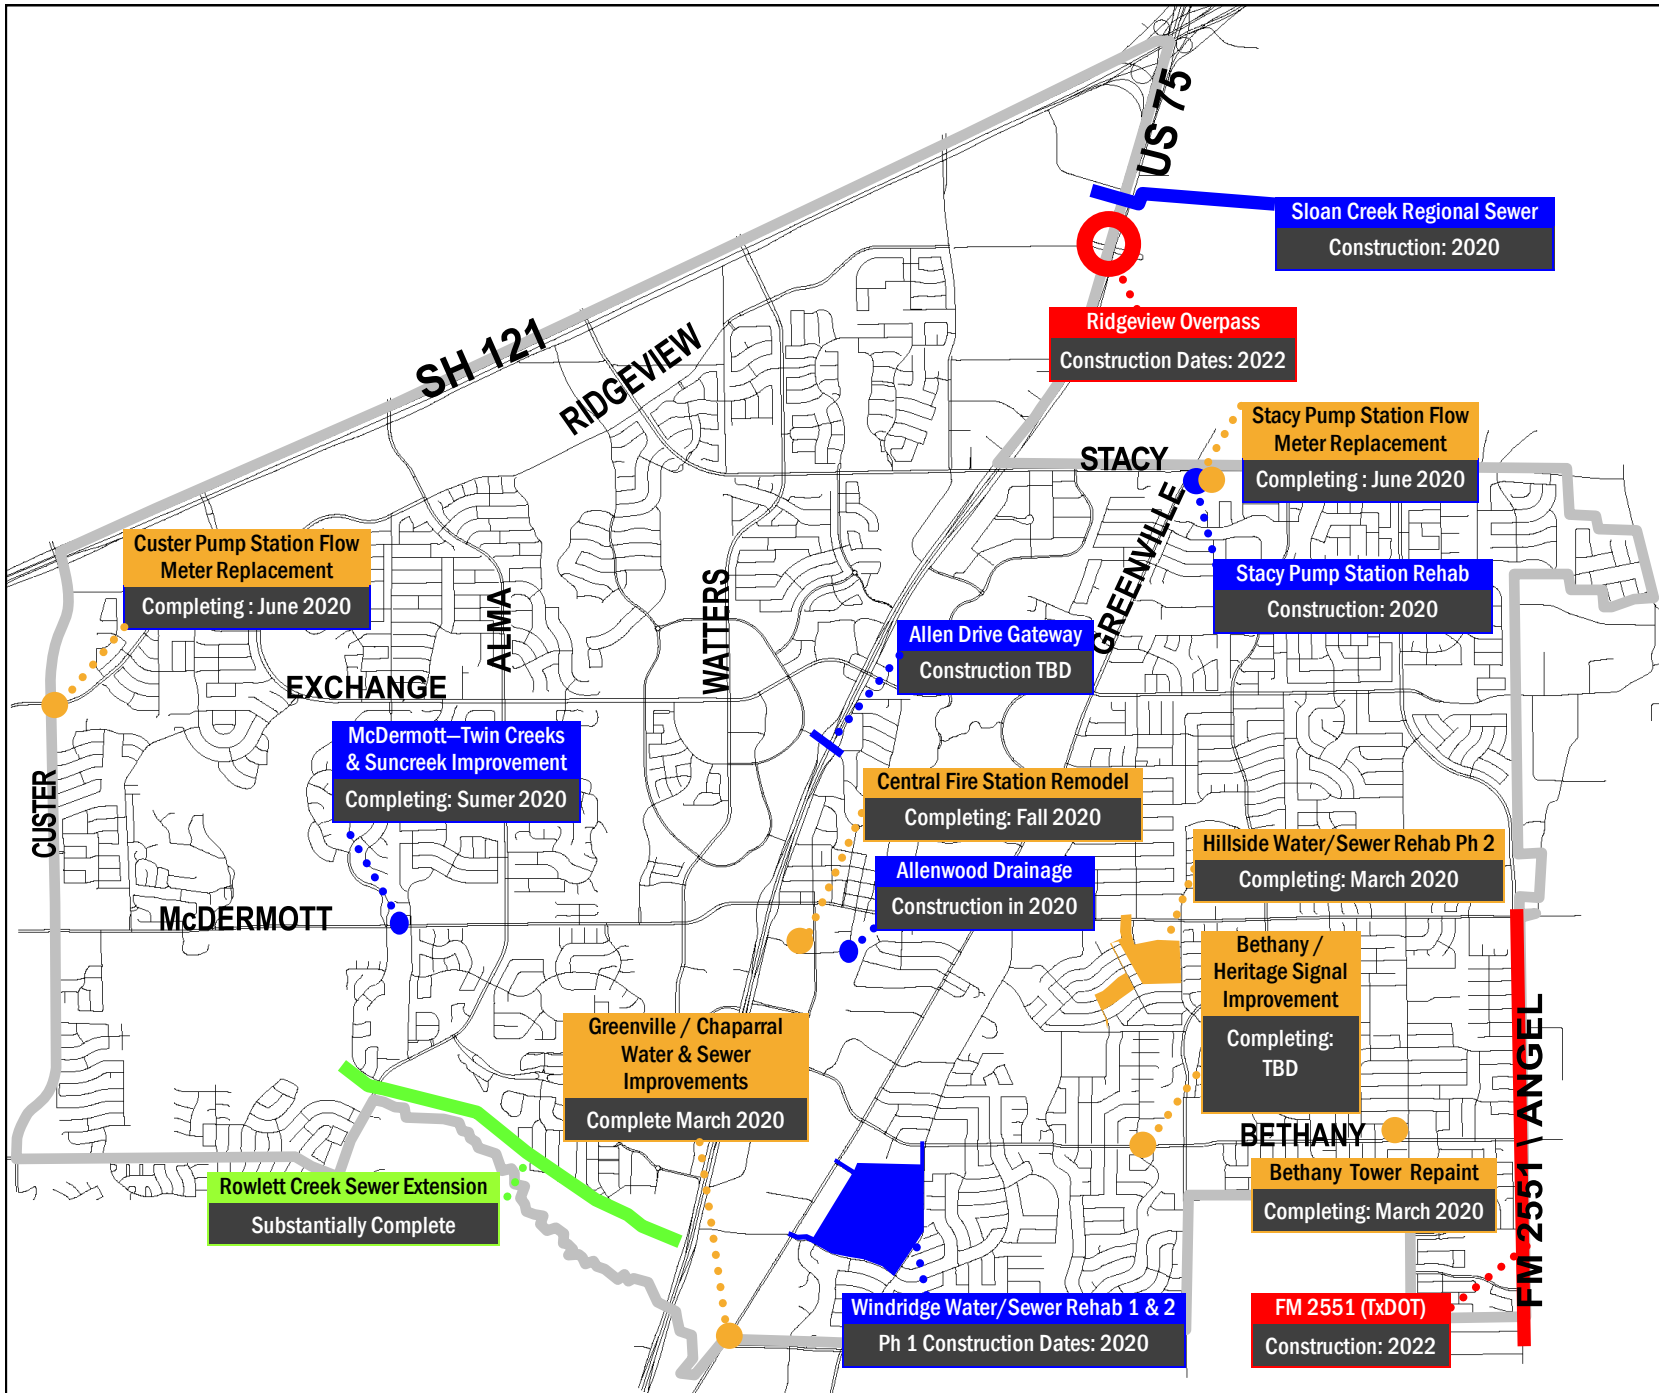

February
2020

CONSTRUCTION

DESIGN

CONSTRUCTION
(By Others)

DESIGN
(By Others)

FUTURE

ENGINEERING
DEPARTMENT
214.509.4576

DIRECTOR:
CHRIS
FLANIGAN

